

Work Order ID 140107

140107

Page 1

Thursday, December 17, 2015 3:42:35 PM

Item ID: D3281-4L02 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Floor Protector, Aft RH (Black)
Start Date: 12/17/2015 Start Qty: 2.00 ***2*** Cust Item ID:
Required Date: 12/17/2015 Req'd Qty: 2.00 ***2*** Customer:
Reference:

Approvals: Process Plan: MLJ Date: DEC 22 2015 Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D3281	Rev F
DSI 9504	A

100		0.00							DEC 17 9-03
100	HAND FINISHING THERMOFORMING					2			16/02/09
Thermoform	Memo	0.00							
Thermoforming Machine	Cut Blanks								

105		0.00							DEC 17 9-03
105	Dry Material					2			16/02/09
HandThermo	Memo	0.00							
Hand Finishing Thermoforming	Dry Sheet as per QSI022 POLYCARBONATE								

Temp: 245 deg. F FEB 09 2016
Time IN: 5:00 PM
Time OUT: 6:00 AM Per: _____

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QS1042) Approval	
Description Work Order Deviation		Disposition			
				Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
☐ OTHER : _____					

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐			
Design ☐	☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐			
Doc/Data ☐	☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐			
Equip/Tooling ☐	☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐			
Handling/Pre ☐	☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐			
Material ☐	☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐			
Internal Transport ☐	☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐			
Tribal Knowledge ☐	☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐			
LOA ☐	☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐			
Substation ☐	☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐			
Past Expiry Date ☐	☐	Manufacturing Process ☐	OTHER :						
Misidentified ☐	☐	Past Due ☐							

Work Order ID 140107

Thursday, December 17, 2015 3:42:35 PM

140107

Page 3

Item ID: D3281-4L02 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Floor Protector, Aft RH (Black)
Start Date: 12/17/2015 Start Qty: 2.00 ***2*** Cust Item ID:
Required Date: 12/17/2015 Req'd Qty: 2.00 ***2*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
150	QC5- Inspect part completeness to step on W/O	0.00							
150									DAS 36
QC	Memo	0.00				(2)			9-88
Quality Control									FEB 10 2016
160	Packaging	0.00							
160									
Packaging	Memo	0.00				2			DAS 6
Packaging									9-88
									FEB 11 2016
170	QC21- Final Inspection - Work Order Release	0.00							
170									
QC	Memo	0.00				MCS			FEB 16 2016
Quality Control									

MCS FEB 11 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS <table style="width:100%; border: none;"> <tr> <td style="width:12.5%;">Skid-tube ☐</td> <td style="width:12.5%;">Cross tube ☐</td> <td style="width:12.5%;">Water Jet ☐</td> <td style="width:12.5%;">Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>						Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐																																					
Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐																																																										
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐																																																										
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐																																																										
Large Fab ☐	Composite ☐	Supplier ☐																																																											
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval																																																						
Description Work Order Deviation				Disposition																																																									
Root Cause <table style="width:100%; border: none;"> <tr><td>Environment ☐</td><td>No Re-verification ☐</td></tr> <tr><td>Design ☐</td><td>Operator ☐</td></tr> <tr><td>Doc/Data ☐</td><td>Offset/Setup ☐</td></tr> <tr><td>Equip/Tooling ☐</td><td>Supplier ☐</td></tr> <tr><td>Handling/Pre ☐</td><td>Training ☐</td></tr> <tr><td>Material ☐</td><td>Use for Testing ☐</td></tr> <tr><td>Internal Transport ☐</td><td>Poor Information ☐</td></tr> <tr><td>Tribal Knowledge ☐</td><td>Rushing ☐</td></tr> <tr><td>LOA ☐</td><td>Product Improvement ☐</td></tr> <tr><td>Substation ☐</td><td>Process Improvement ☐</td></tr> <tr><td>Past Expiry Date ☐</td><td>Manufacturing Process ☐</td></tr> <tr><td>Misidentified ☐</td><td>Past Due ☐</td></tr> </table>		Environment ☐	No Re-verification ☐	Design ☐	Operator ☐	Doc/Data ☐	Offset/Setup ☐	Equip/Tooling ☐	Supplier ☐	Handling/Pre ☐	Training ☐	Material ☐	Use for Testing ☐	Internal Transport ☐	Poor Information ☐	Tribal Knowledge ☐	Rushing ☐	LOA ☐	Product Improvement ☐	Substation ☐	Process Improvement ☐	Past Expiry Date ☐	Manufacturing Process ☐	Misidentified ☐	Past Due ☐	FAULT CATEGORY <table style="width:100%; border: none;"> <tr> <td style="width:33%;">Pressure/Forced ☐</td> <td style="width:33%;">Temperature/Cure ☐</td> <td style="width:33%;">Power Loss/Surge ☐</td> </tr> <tr> <td>Bending ☐</td> <td>Set-up ☐</td> <td>Folio/Program ☐</td> </tr> <tr> <td>Centre Not Concentric ☐</td> <td>BOM/Route ☐</td> <td>Grain ☐</td> </tr> <tr> <td>Cracks ☐</td> <td>Broken/Damage/Defect ☐</td> <td>Weld ☐</td> </tr> <tr> <td>Crimp/Kink/Ripple/Wave ☐</td> <td>Inspection Incomplete/Unqualified ☐</td> <td>Wrong Stock Pulled ☐</td> </tr> <tr> <td>Cuffs ☐</td> <td>Contamination ☐</td> <td>Out of Sequence ☐</td> </tr> <tr> <td>Crushing ☐</td> <td>Countersink ☐</td> <td>Off-set ☐</td> </tr> <tr> <td>Heat Treat ☐</td> <td>Cut Too Short ☐</td> <td>Mislabeled ☐</td> </tr> <tr> <td>Wave/Twist in Tube ☐</td> <td>Instructions Incomplete/Unclear ☐</td> <td>Fit/Function ☐</td> </tr> <tr> <td>Marks/Chatter ☐</td> <td>Drill Holes ☐</td> <td>Misaligned/off center ☐</td> </tr> </table>						Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Crushing ☐	Countersink ☐	Off-set ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐
Environment ☐	No Re-verification ☐																																																												
Design ☐	Operator ☐																																																												
Doc/Data ☐	Offset/Setup ☐																																																												
Equip/Tooling ☐	Supplier ☐																																																												
Handling/Pre ☐	Training ☐																																																												
Material ☐	Use for Testing ☐																																																												
Internal Transport ☐	Poor Information ☐																																																												
Tribal Knowledge ☐	Rushing ☐																																																												
LOA ☐	Product Improvement ☐																																																												
Substation ☐	Process Improvement ☐																																																												
Past Expiry Date ☐	Manufacturing Process ☐																																																												
Misidentified ☐	Past Due ☐																																																												
Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐																																																											
Bending ☐	Set-up ☐	Folio/Program ☐																																																											
Centre Not Concentric ☐	BOM/Route ☐	Grain ☐																																																											
Cracks ☐	Broken/Damage/Defect ☐	Weld ☐																																																											
Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐																																																											
Cuffs ☐	Contamination ☐	Out of Sequence ☐																																																											
Crushing ☐	Countersink ☐	Off-set ☐																																																											
Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐																																																											
Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐																																																											
Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐																																																											
		OTHER : ☐																																																											

Picklist Print

Thursday, December 17, 2015 3:42:35 PM

Page 1

Work Order ID: 140107

140107

Parent Item: D3281-4L02

D3281-4L02

Parent Item Name: Floor Protector, Aft RH (Black)

Start Date: 12/17/2015

Required Date: 12/17/2015

Start Qty: 2.00

Required Qty: 2.00

Comments:

IPP Rev:A04.07.01New issueKJ/JLM

IPP Rev B 07.08.07 Thermoform in house DL

ADD Step 105 Dry Material 10/04/21 DL

IPP Rev. C

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
MLEXS.093-F6006-02		Purchased					sf	1,032.737		8.666			07 9-03
MI FXS 093-F6006-02													
GE PLASTICS LEXAN SHEET													

Location

Loc Qty

Loc Code

therm

m127208

1032.73737

1032.73737

8.675g H.

16/02/09

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date : _____		Step #: _____		QTY Effective : _____			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
		OTHER : ☐							

DART AEROSPACE LTD		Work Order:	140107
Description: Floor Protector, Aft RH		Part Number:	D3281-4
Inspection Dwg: D3281	Rev: F	Page 1 of 1	

FIRST ARTICLE INSPECTION CHECKLIST
THERMOFORMING SECTION

Description	Accept	Reject	Method of Inspection	Comments
Inside Radii less than 0.1875"	✓			
Shape Definition	✓			
Texture Retention	✓			
Material imperfections such as bumps, cracks, voids, scratching	✓			

Measured by: ^{DAS}
07
9-89

Date: 16/02/09

TRIMMING SECTION

Drawing Dimension	Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
17.8	+/-0.100	17.7"	✓			
17.1	+/-0.100	17.0"	✓			
14.3	+/-0.100	14.3"	✓			
0.95	+/-0.030	0.956"	✓			
0.050	Min	0.068"	✓			
0.070	Min	0.084"	✓			

Measured by: ^{DAS}
07

Date: 16/02/09

Audited by: ^{9-89 DAS}
38

Date: FEB 10 2016

Preliminary Approval: ⁹⁻⁸⁹

Date:

Rev	Date	Change	Revised by	Approved
A	08.02.28	New Issue	KJ/DL	
B	08.04.16	Dimensions updated per Dwg Rev D	KJ/DL	
C	10.09.01	Dimensions updated per Dwg Rev E	KJ	
D	11.06.21	Dwg Rev updated	KJ	


8 7 6 5 4 3 2 1

D

C

B


A

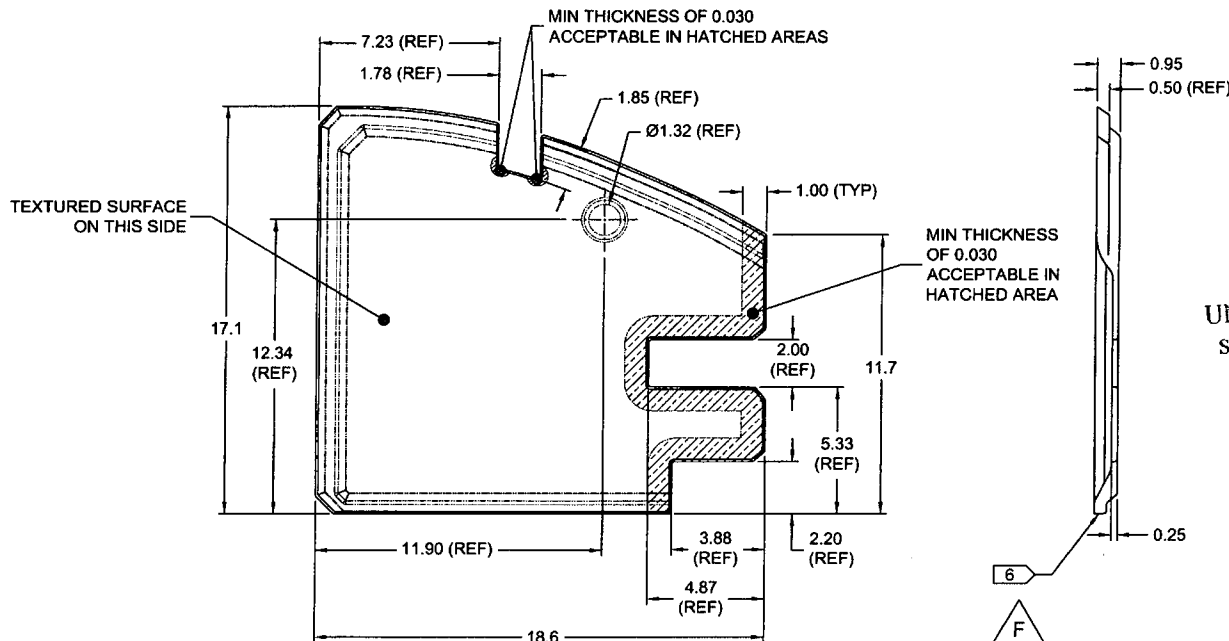

D3281-1 FLOOR PROTECTOR

NOTES:

- 1) MATERIAL: -1L02 = LEXAN F6006, BLACK No. 701, 0.093" THICK (MLEXS.093-F6006-02)
-1L08 = LEXAN 90318 (PROTECT-A-GLAZE), 0.118 THICK, 112-CLEAR (MLEXS.118-90318-08)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.010 MAX
- 6) IDENTIFICATION: IDENT WITH DART P/N "D3281-1Lxx" AND B/N PER QSI 044 6.4 ALONG PERIMETER OF PART AS SHOWN.
- 7) WEIGHT: D3281-1L02 = 0.95 lb D3281-1L08 = 1.13 lb
- 8) THERMOFORM WITH MOLD D3281-1T1 PER DART QSI 022; TRIM AS SHOWN
MINIMUM THICKNESS AFTER FORMING: 0.070" EXCEPT WHERE INDICATED

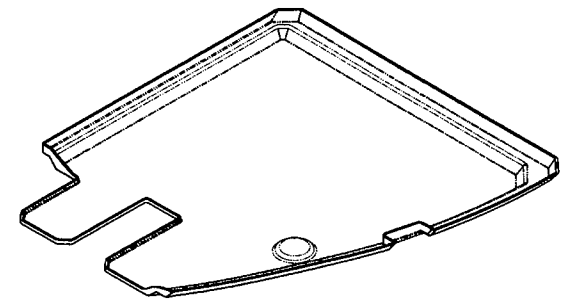

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 14-0107-MJS

1512-22R RELEASED
2010-11-25

F	NOTES UPDATED. FLAG NOTE 6 WAS 7 & RELOC. D.E.O. D3281-E-1 INC. DIM 17.0 WAS 17.1 (ZN B5-3, B6-4) & 17.7 WAS 17.8 (ZN C5-3, C6-4) REF CAR 10-21.	JPH	10.09.27
E	3/4" NOW TRIMMED FLAT: RMV 0.25 BEVEL TO FACILITATE TRIMMING (ZN D6-3, D4-4)	CP	10.01.05
D	THICKNESS 0.093 WAS 0.125, MIN THICKNESS 0.070 WAS 0.080, P/N AND B/N ID WITH VIBRATING STYLUS (ZN A7-1, A7-2, A7-3, A7-4); D3281-4 NOW ON PAGE 4; CORRECT WEIGHTS (ZN A8-1, A8-2, A8-3, A8-4)	PH	08.03.28
C	UPDATE DIMS TO MATCH PARTS: COLOUR 701 WAS 700; GENERAL UPDATE	LE	07.10.09
B	NOW LEXAN; DIMS AS MANUFACTURED	CP	05.11.25
A	NEW ISSUE	CP	04.05.03
REV.	DESCRIPTION	BY	DATE
DESIGN			
DRAWN			
CHECKED			
MFG. APPR.			
APPROVED			
DE APPR.			
DATE	10.09.27		

DART AEROSPACE LTD
HAWKESBURY, ONTARIO, CANADA

DRAWING NO. REV. F
D3281 SHEET 1 OF 4
TITLE SCALE
FLOOR PROTECTOR NTS

COPYRIGHT © 2004 BY DART AEROSPACE LTD
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.




D

C

B

A

8 7 6 5 4 3 2 1

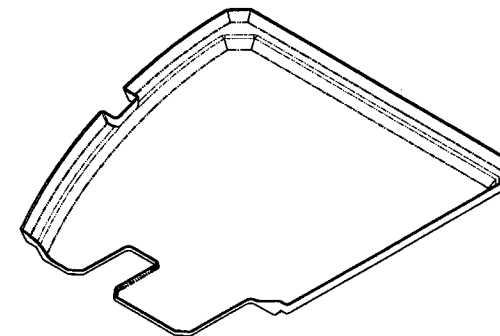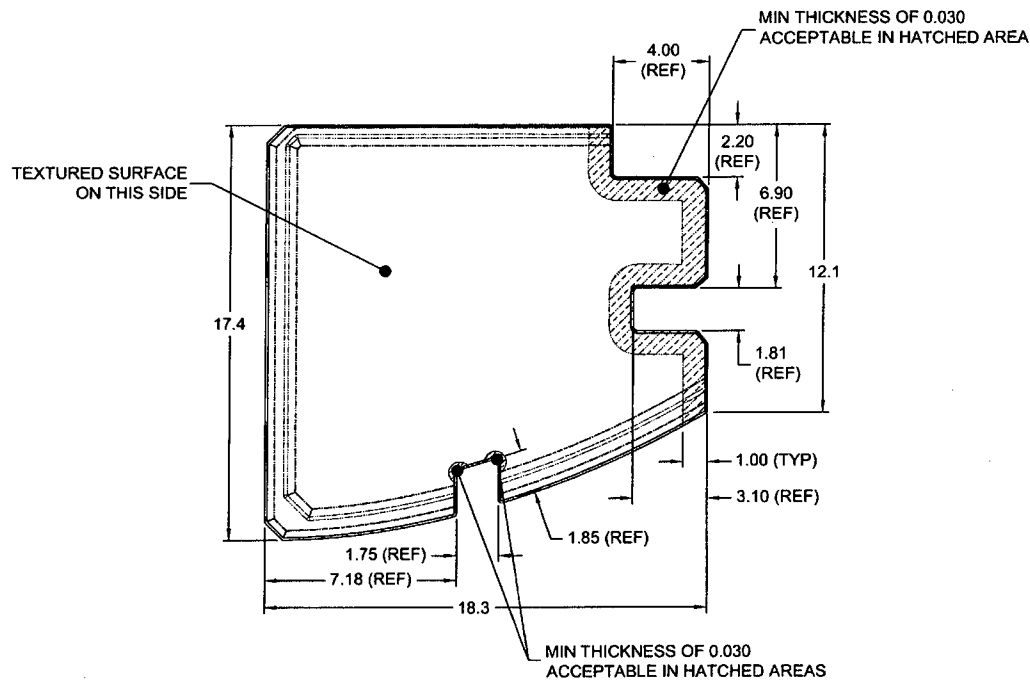



D3281-2 FLOOR PROTECTOR

NOTES:

- 1) MATERIAL: -2L02 = LEXAN F6006, BLACK No. 701, 0.093" THICK (MLEXS.093-F6006-02)
-2L08 = LEXAN 90318 (PROTECT-A-GLAZE), 0.118 THICK, 112-CLEAR (MLEXS.118-90318-08)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.010 MAX
- 6) IDENTIFICATION: IDENT WITH DART P/N "D3281-2Lxx" AND B/N PER QSI 044 6.4 ALONG PERIMETER OF PART AS SHOWN.
- 7) WEIGHT: D3281-2L02 = 0.95 lb D3281-2L08 = 1.13 lb
- 8) THERMOFORM WITH MOLD D3281-2T1 PER DART QSI 022; TRIM AS SHOWN
MINIMUM THICKNESS AFTER FORMING: 0.070" EXCEPT WHERE INDICATED

RELEASED
2010-11-25

DESIGN	90	DART AEROSPACE LTD	
DRAWN	JP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	JP	DRAWING NO.	REV. F
MFG. APPR.	JP	D3281	SHEET 2 OF 4
APPROVED	JP	TITLE	SCALE
DE APPR.	JP	FLOOR PROTECTOR	NTS
DATE	10.09.27	COPYRIGHT © 2004 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

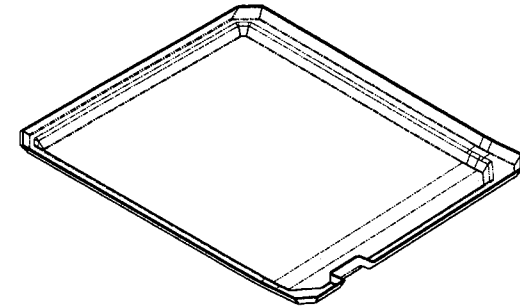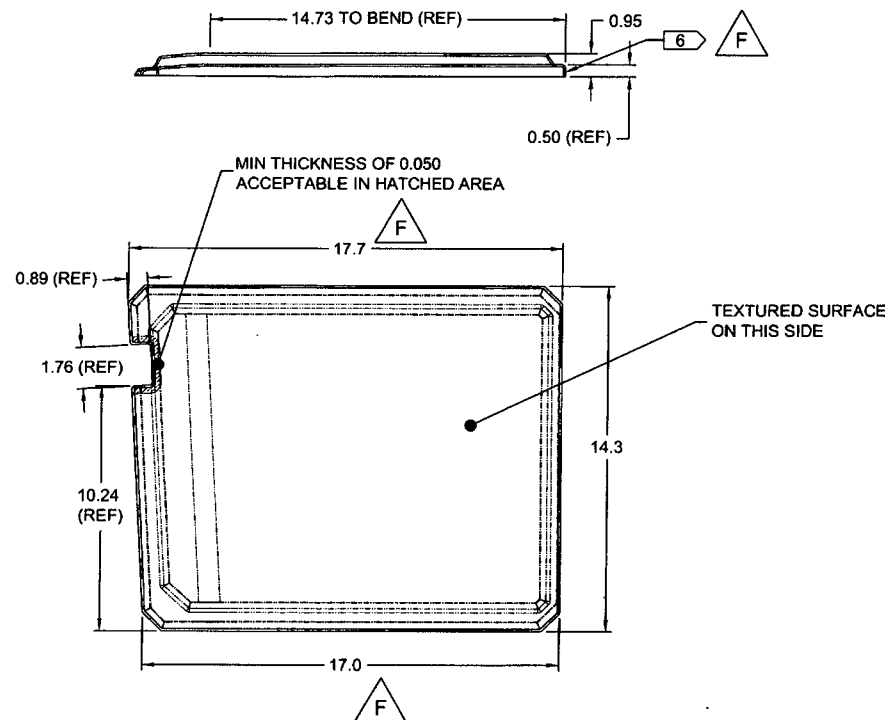




D3281-3 FLOOR PROTECTOR

NOTES:

- 1) MATERIAL: -3L02 = LEXAN F6006, BLACK No. 701, 0.093" THICK (MLEXS.093-F6006-02)
-3L08 = LEXAN 90318 (PROTECT-A-GLAZE), 0.118 THICK, 112-CLEAR (MLEXS.118-90318-08)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.010 MAX
- 6) IDENTIFICATION: IDENT WITH DART P/N "D3281-3Lxx" AND B/N PER QSI 044 6.4 ALONG PERIMETER OF PART AS SHOWN.
- 7) WEIGHT: D3281-3L02 = 0.87 lb D3281-3L08 = 1.05 lb
- 8) THERMOFORM WITH MOLD D3281-3T1 PER DART QSI 022; TRIM AS SHOWN
MINIMUM THICKNESS AFTER FORMING: 0.070" EXCEPT WHERE INDICATED

RELEASE
2010-11-25

DESIGN		DART AEROSPACE LTD	
DRAWN		HAWKESBURY, ONTARIO, CANADA	
CHECKED		DRAWING NO.	REV. F
MFG. APPR.		D3281	SHEET 3 OF 4
APPROVED		TITLE	SCALE
DE APPR.		FLOOR PROTECTOR	NTS
DATE	10.09.27	COPYRIGHT © 2004 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

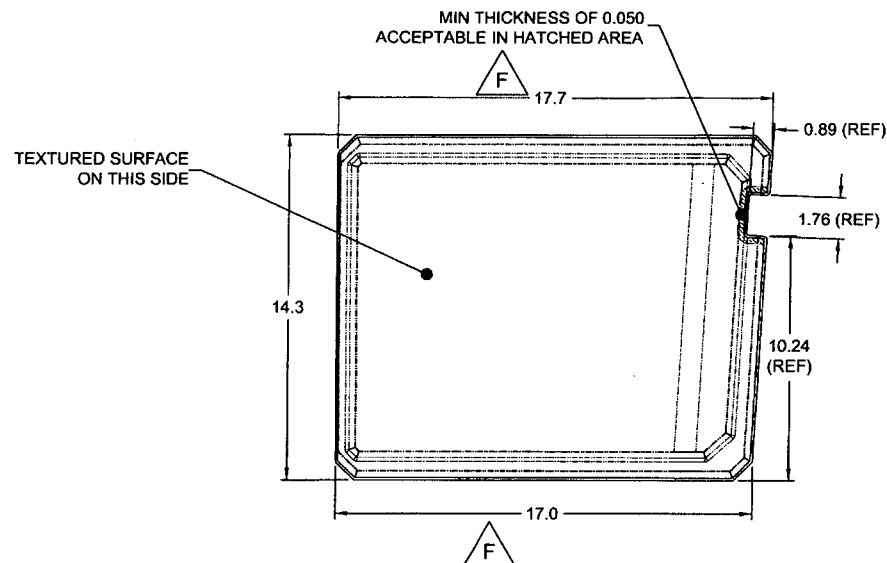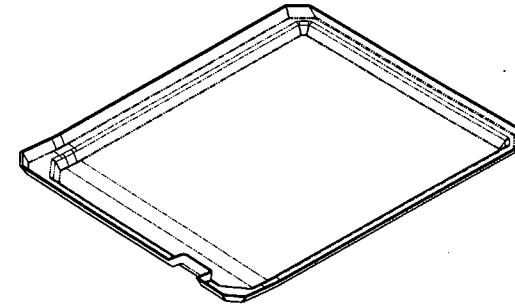

D3281-4 FLOOR PROTECTOR

D3281-4 NOTES:

- 1) MATERIAL: -4L02 = LEXAN F6006, BLACK No. 701, 0.093" THICK (MLEXS.093-F6006-02)
-4L08 = LEXAN 90318 (PROTECT-A-GLAZE), 0.118 THICK, 112-CLEAR (MLEXS.118-90318-08)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.010 MAX
- 6) IDENTIFICATION: IDENTIFICATION: IDENT WITH DART P/N "D3281-4Lxx" AND B/N PER QSI 044 6.4 ALONG PERIMETER OF PART AS SHOWN.
- 7) WEIGHT: D3281-4L02 = 0.87 lb D3281-4L08 = 1.05 lb
- 8) THERMOFORM WITH MOLD D3281-4T1 PER DART QSI 022; TRIM AS SHOWN
MINIMUM THICKNESS AFTER FORMING: 0.070" EXCEPT WHERE INDICATED

RELEASE
2010-11-25

DESIGN		DART AEROSPACE LTD	
DRAWN		HAWKESBURY, ONTARIO, CANADA	
CHECKED		DRAWING NO.	REV. F
MFG. APPR.		D3281	SHEET 4 OF 4
APPROVED		TITLE	SCALE
DE APPR.		FLOOR PROTECTOR	NTS
DATE	10.09.27	COPYRIGHT © 2004 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	
